

Business Requirements Document (BRD)

eCourts Phase III PMIS
24th June 2026
Version 3

KPMG Internal PMIS Configuration
Prepared by: KPMG PMU Support Team
Draft — Internal Use On

Table of Contents

Table of Contents	2
1. Purpose & Background	3
1.1 Document Objective	3
1.2 Reporting Coverage	3
2. Scope	3
2.1 In Scope	3
2.2 Out of Scope	4
3. Solution Overview	Error! Bookmark not defined.
3.1 Building Blocks	4
3.2 Record Grain (Summary)	5
4. Trackers & Form Fields	5
4.1 Physical Tracker	5
4.1.1 Form Fields — Physical Entry	5
4.1.2 Indicator Catalogue (illustrative — full list from master)	6
4.2 Financial Tracker	6
4.2.1 Form Fields — Financial Entry	6
4.3 Outcome Tracker	7
4.3.1 Form Fields — Outcome Entry	7
4.3.2 Subject & KPI Catalogue (illustrative — full list from master)	8
5. Data Model	8
5.1 Reporting Period Structure	8
5.2 Common Reporting Dimensions	9
6. Validation & Business Rules	9
7. Master Data	9
7.1 Components (17)	9
7.2 Other Master Lists	10
8. User Creation & Role Definition	10
8.1 Roles	10
8.2 User Lifecycle	11
9. Reporting Structures (PMIS)	11
9.1 Tracker Report Views	11
9.2 Filters & Interaction	12
9.3 Scope Enforcement in Reports	12
10. Non-Functional Requirements	13
11. Key Assumptions & Dependencies	13
12. Glossary	13

1. Purpose & Background

This Business Requirements Document (BRD) defines the requirements for the **eCourts Phase III Project Monitoring Information System (PMIS)** - a structured, web-based tool through which the Department of Justice (DoJ) and the Project Monitoring Unit (PMU) will capture, validate, store and report progress of the scheme across all 28 High Courts and 17 sanctioned components.

The PMIS replaces the current practice of collecting progress through monthly PDF/Excel returns. It establishes a single data source built around three trackers - **Physical**, **Financial** and **Outcome** - each with its own indicators, form fields and validation rules.

1.1 Document Objective

This BRD is prepared by the PMU Support Team on behalf of DoJ and is submitted to the KPMG PMIS Development Team for onward build. It is intended to be sufficient for the development team to configure the data-capture forms, trackers, reporting structures, user accounts and role-based access without further functional clarification.

1.2 Reporting Coverage

- **Baseline:** Cumulative progress from September 2023 to May 2026 is entered as the opening dataset at go-live - one consolidated record per High Court per component per tracker.
- **Going forward:** From June 2026, data is captured monthly - one record per High Court per component (or per KPI, for the Outcome Tracker) per calendar month.

Note. All figures appearing in the companion wireframe/prototype are dummy values for design reference only. Actual figures will reflect live PMIS data once High Courts begin entering updates.

2. Scope

2.1 In Scope

#	PMIS Capability - In Scope
1	Physical Tracker - indicator-level data capture for all 17 components
2	Financial Tracker - component-level funds released & utilized
3	Outcome Tracker - Subject → KPI capture (Absolute / Relative), with State / District / National granularity
4	Data-entry forms for each tracker, replacing the offline returns
5	Master data management (High Courts, Components, Indicators, KPIs, Units of Measure)
6	Validation rules and duplicate prevention
7	User creation, role definition and Role-Based Access Control (RBAC)
8	State (High Court) scoping - CPC users restricted to their own jurisdiction
9	Reporting structures - listing, filtering, drill-down tables and export (Excel / PDF)
10	Audit trail / change log on every edit
11	Global Dashboard

#	PMIS Capability - In Scope
12	KPI cards and charts (Summary, clustered bar, RAG visuals)
13	Additional Trackers to be added later – PMU Task Tracker; DPR Deliverables Tracker
14	District-court-level onboarding (data model must remain extensible for it later)

2.2 Out of Scope

#	Out of Scope (for this BRD)
1	Procurement of any new tool or platform — PMIS is configured within existing infrastructure

3. Solution Overview

The PMIS is organised as three trackers sharing a common reporting backbone (period, High Court, component) and a common access-control layer. Users sign in once; what they can see and do is governed by their role and, for CPC users, their assigned High Court.

3.1 Building Blocks

Building Block	Purpose
Login & Authentication	Single secure sign-in for all user types; session scoped by role and jurisdiction.
Physical Tracker	Captures indicator-level physical progress (Target vs Achieved) for each component.
Financial Tracker	Captures funds released and funds utilised per component, with derived utilisation and variance.
Outcome Tracker	Captures DPR outcome KPIs (Absolute / Relative) at State / District / National granularity.
Master Data	Authoritative lists: High Courts, Components, Indicators, KPIs, Units of Measure.
RBAC & User Management	Admin creates users, assigns roles and jurisdictions; CPCs are scoped to their own High Court.
Reporting & Export	Filterable, sortable tables per tracker with Excel / PDF export
Audit Trail	Every create/edit logged with user, timestamp, field, old value and new value.
Global Dashboard	Dashboard providing bird's eye view of the financial and physical performance of the project

Sign in to PMIS

Select your access level and enter your credentials.

Admin - DOJ / PMU
All-India view, all High Courts

CPC - High Court
Own State data only

User ID / e-Mail

admin.pmu@doj.gov.in

Password

Sign in securely →

[Forgot password?](#)
[NIC SSO enabled](#)

3.2 Record Grain (Summary)

Tracker	One record per...	Entered by
Physical	High Court × Component × Indicator × Reporting Month	CPC (own HC); Admin (any HC)
Financial	High Court × Component × Reporting Month	CPC (own HC); Admin (any HC)
Outcome	Granularity unit × Subject × KPI × Reporting Month	CPC (own HC); Admin (any HC)

Data-entry ownership is locked as follows: **the CPC (High Court) user enters all values for their own High Court; the Admin (DoJ / PMU) may enter or override values for any High Court.**

4. Trackers & Form Fields

Each tracker is a separate, highly detailed data-capture sheet. This section defines, for every tracker, the indicators/KPIs to be captured, the form fields, their data types and entry behaviour. Field-level validation common to all trackers is consolidated in Section 6.

4.1 Physical Tracker

The Physical Tracker captures progress at the indicator level. Each of the 17 components has one or more indicators; for every indicator the user records a Target (set centrally) and an Achieved value (cumulative as of the reporting month). The system derives % Achieved and a RAG status.

4.1.1 Form Fields — Physical Entry

Field	Type	Entry	Notes
Reporting Month	MM/YYYY	Select	Drives period filter; cannot be a future month.
High Court / Bench	List	Select / scoped	CPC fixed to own HC; Admin selects any.
Component	List	Select	One of 17 (master list).
Indicator / Description	List	Select	Indicator under the chosen component (master list).
Data Type	Int / Float	Auto	From indicator master (e.g. counts = Int, pages in Cr = Float).

Field	Type	Entry	Notes
Unit / Validation	Text	Auto	e.g. 'Absolute count (numbers)', 'in Cr.'
Target	Number	Admin only	Read-only for CPC; set by DoJ / PMU.
Achieved	Number	Enter	Cumulative achievement as of reporting month.
% Achieved	Number	Derived	$(\text{Achieved} \div \text{Target}) \times 100$.
Status (RAG)	Flag	Derived	Green $\geq 80\%$ · Amber 65–79% · Red $< 65\%$.
Remarks	Text	Enter	Optional free text.

4.1.2 Indicator Catalogue (illustrative — full list from master)

The PMIS must support the full indicator catalogue defined in the project tracker. A representative extract is shown below; the complete list is supplied as master data (Section 7).

Component	Indicators (examples)	Data Type
e-Sewa Kendras	Sites prepared; kendras in court complexes; kendras functional; porta-cabin set-up; functional internet	Int
Paperless Courts	Paperless courts; court rooms with VC / LED / scanner / computer / speech-to-text	Int
Expansion of Virtual Courts	Sites prepared; virtual courts operational; document visualisers installed	Int
Live Streaming	Sites prepared; court rooms enabled; LED / scanner / computer deployed	Int
Digitisation of Court Records	Pages digitised; active-case pages; legacy-case pages (all in Cr.)	Float
Video Conferencing Upgrade	VC units installed / functional; VC in hospitals / jails / courts + DSA	Int
Solar Power for ICT	Solar panels installed	Int
NSTEP Expansion	Court establishments covered; hand-held devices deployed	Int
e-Office for HC & District Courts	Courts that implemented e-Office	Int

4.2 Financial Tracker

The Financial Tracker captures funds released, and funds utilised for each component. The system derives utilisation percentage and variance. Figures are in ₹ Crore.

4.2.1 Form Fields — Financial Entry

Field	Type	Entry	Notes
Reporting Month	MMM YYYY	Select	Cannot be a future month.
High Court / Bench	List	Select / scoped	CPC fixed to own HC; Admin any.
Component	List	Select	One of 17.
Description / UoM	Text	Auto	From component master.

Field	Type	Entry	Notes
Funds Released (₹ Cr)	Float	Enter	Cumulative funds released as of reporting month.
Funds Utilised (₹ Cr)	Float	Enter	Cumulative funds utilised as of reporting month.
Utilisation %	Number	Derived	$(\text{Funds Utilised} \div \text{Funds Released}) \times 100$.
Variance (₹ Cr)	Number	Derived	Funds Released – Funds Utilised.
Status (RAG)	Flag	Derived	Based on Utilisation % thresholds.
Remarks	Text	Enter	Optional.

Entry ownership. Per the locked model, the CPC enters both Funds Released and Funds Utilised for their own High Court, and the Admin (DoJ / PMU) may enter or override either value for any High Court.

The screenshot displays the 'Enter Financial Data' interface within the eCourts Phase III PMIS. The sidebar on the left contains navigation links for Overview, Trackers, Data Capture, and Administration. The main content area is titled 'Enter Financial Data' and includes a note that Admin can record both funds released and utilisation for any High Court. It features a table with 17 components for financial entries, showing fields for Funds Released and Utilisation for various categories like e-Sewa Kendras, Paperless Courts, Expansion of Virtual Courts, Live Streaming, Digitization of Court Records, Video Conferencing Upgrade, and Solar Power for ICT.

4.3 Outcome Tracker

The Outcome Tracker captures the outcome KPIs defined in the eCourts DPR. Its structure differs from the Physical and Financial trackers: outcomes are organised as **Subject** → **KPI**, each KPI being either **Absolute** (a count or amount) or **Relative** (a value measured against a stated baseline), and captured at a defined granularity (State, District or National).

4.3.1 Form Fields — Outcome Entry

Field	Type	Entry	Notes
Reporting Month	MMM YYYY	Select	Honours the KPI's periodicity (monthly / cumulative / yearly / on-date).
Granularity Unit	List	Select / scoped	State / District / National per KPI; CPC scoped to own HC's State & districts.
Subject	List	Select	One of 19 subject areas (e.g. eFiling, ICJS, ePay).
KPI ID	Code	Auto	e.g. 1.01, 4.2 (from KPI master).

Field	Type	Entry	Notes
Key Process / Outcome	Text	Auto	KPI description from master.
Outcome Type	Abs / Rel	Auto	Absolute or Relative (from master).
Baseline	Text / Number	Auto / Enter	Denominator for Relative KPIs (e.g. 'Bar-enrolled advocates').
Value Type	List	Auto	Percentage / Count / Amount / Ratio.
Value	Number	Enter	The reported value for the period.
Computed %	Number	Derived	For Relative KPIs: $(\text{Value} \div \text{Baseline}) \times 100$.
Remarks	Text	Enter	Optional.

4.3.2 Subject & KPI Catalogue (illustrative — full list from master)

#	Subject	Example KPIs	Granularity
1	eFiling	Advocates on-boarded; new cases filed & verified; documents submitted	District
2	Automated eMail	Advocate eMail IDs provided; eMails sent per month	State / District
3	SMS	SMS sent to advocates & litigants; mobile numbers provided	State / National
4	ICJS	FIR consumed / verified; chargesheet consumed / verified	District
5	NSTEP	Bailiffs on-boarded; civil/criminal process published & served	District
6	Virtual Courts	Challans received; cases completed; fine collected	State
7	ePay	Court fee / fine / penalty paid online; transaction value	District
8	Mobile App	Android / iOS downloads; case status accessed	National
9	Video Conferencing	Hearings via VC (civil / criminal); downtime incidents	District
12	DC Services Portal	Orders & judgements uploaded; digitally signed orders	District / National
16	eOffice	Staff on-boarded; eFiles processed; receipts	State
18	Change Management	Judicial officers / staff / advocates trained; training hours	State / District

Coverage. The catalogue spans 19 subject areas of the DPR. The complete KPI master - including KPI ID, outcome type, baseline, value type and periodicity - is supplied as master data and must be loaded before go-live.

5. Data Model

5.1 Reporting Period Structure

- **Baseline record (Sep 2023 – May 2026):** one consolidated entry per High Court per component (and per KPI for Outcome), loaded as the opening dataset at go-live.
- **Monthly records (Jun 2026 onwards):** one record per High Court per component (or KPI) per calendar month.

5.2 Common Reporting Dimensions

Dimension	Description	Source
Reporting Month	Calendar month the record covers (MMM YYYY)	Selected at entry
High Court / Bench	Reporting unit (28 values)	Master list
Component	One of 17 sanctioned components	Master list
Indicator / KPI	Indicator (Physical) or KPI (Outcome) under the component / subject	Master list
Granularity	State / District / National (Outcome only)	KPI master

6. Validation & Business Rules

1. Target, Description / Unit of Measure, Data Type and KPI metadata are read-only for CPC users; only Admin (DoJ / PMU) may change them.
2. Achieved, Funds Released, Funds Utilised and Outcome Values must be numeric and cannot be negative.
3. If Funds Utilised exceeds Funds Released for an entry, the system shows a warning but does not block submission (corrections may follow).
4. No duplicate records: each combination of High Court + Component + Indicator/KPI + Reporting Month must be unique.
5. Reporting Month cannot be set to a future month.
6. Relative Outcome KPIs require a baseline; if the baseline is zero or missing, the computed percentage is suppressed rather than shown as an error.
7. Derived fields (% Achieved, Utilisation %, Variance, RAG status, Computed %) are system-calculated and never directly editable.
8. Every create or edit is written to the audit trail with user, timestamp, field, old value and new value (Section 10).

RAG thresholds. Default status bands — Green $\geq 80\%$, Amber 65–79%, Red $< 65\%$ — apply to % Achieved and Utilisation %. Thresholds must be configurable by Admin.

7. Master Data

The following master lists must be loaded and maintained in the PMIS. All are table-driven and editable by Admin only.

7.1 Components (17)

#	Component	Primary Unit of Measure
1	e-Sewa Kendras	No. of e-sewa kendras in court complexes
2	Paperless Courts	No. of paperless courts
3	Expansion of Virtual Courts	No. of virtual courts
4	Live Streaming	No. of courts
5	Digitisation of Court Records	No. of pages digitised (in Cr.)

#	Component	Primary Unit of Measure
6	Video Conferencing Upgrade	No. of VC units
7	Solar Power for ICT	Total power generated (kWh)
8	Additional Hardware (Ph I & II)	No. of courts
9	ICT for Newly Set-Up Courts	No. of courts
10	HC & DC Website Migration (S3WaaS)	No. of District Court websites
11	Cloud Computing & Storage	Total centralised storage (PB)
12	ICT Training / Change Management	No. of training programmes
13	NSTEP Expansion	No. of court establishments
14	Software Development	No. of receipts
15	PMU in e-Committee & DoJ	% of project targets achieved
16	Connectivity (Primary + Redundancy)	No. of court complexes
17	e-Office for HCs & District Courts	No. of e-office installations

7.2 Other Master Lists

- **High Courts / Benches (28):** official reporting-unit list (Refer Annexure 4)
- **Physical Indicators:** full indicator catalogue per component, with data type and validation/UoM. (Refer Annexure 1)
- **Financial Indicators:** full indicator catalogue per component, with value type and validation. (Refer Annexure 2)
- **Outcome Subjects (19) & KPIs:** KPI ID, outcome type (Absolute/Relative), baseline, value type and periodicity. (Refer Annexure 3)

8. User Creation & Role Definition

Access to the PMIS is governed by Role-Based Access Control (RBAC). Admin creates user accounts and assigns each a role and, for CPC users, a single High Court jurisdiction.

8.1 Roles

Role	Tentative count	Who	Capabilities
Admin (DoJ / PMU)	10	DoJ nodal team, PMU administrators	Full system control; create / delete accounts; reset passwords; manage master data; set targets; enter or override any High Court's data; configure thresholds; access all files, logs and backups.
CPC (High Court)	28	High Court ICT cell / Central Project Coordinator	Enter and edit all values for own High Court across all three trackers; view own HC's data and reports only; every edit timestamped and logged; cannot see other High Courts.

Role	Tentative count	Who	Capabilities
Viewer	-	e-Committee Secretariat, reviewers	Read-only across permitted scope; can view data and reports; cannot create, edit, delete or modify anything.

8.2 User Lifecycle

- Admin creates an account, assigns a role and (for CPC) a High Court.
- Credentials are issued; standard PMIS login applies; password reset is an Admin function.
- Role or jurisdiction changes are audit-logged with effective date.


9. Reporting Structures (PMIS)

Reporting within the PMIS is tabular. The PMIS provides the structured, filterable, exportable tables that feed both day-to-day monitoring and the downstream Dashboard.

9.1 Tracker Report Views

Report	Grain	Key Columns
Physical Report	HC × Component × Indicator	Target, Achieved, % Achieved, RAG, Remarks
Financial Report	HC × Component	Funds Released, Funds Utilised, Utilisation %, Variance, RAG
Outcome Report	Granularity × Subject × KPI	Type, Baseline, Value, Computed %, Periodicity

Indicator / Description	Data Type	Target	Achieved	Progress	Status
e-Seva Kendras					
No. of sites prepared	Int	420	366	87%	87%
No. of e-sewa kendras in court complexes	Int	390	341	87%	87%
No. of e-sewa kendras functional	Int	390	318	82%	82%
No. of e-sewa kendras set up with porta cabin	Int	150	121	81%	81%
No. of e-sewa kendras within existing complex	Int	240	197	82%	82%
No. of e-sewa kendras with functional internet	Int	390	329	84%	84%
Paperless Courts					
No. of paperless courts	Int	1,200	924	77%	77%
No. of court rooms with VC enabled	Int	1,200	1,011	84%	84%
No. of court rooms with LED display	Int	1,200	872	73%	73%
No. of court rooms with scanner deployed	Int	1,200	905	75%	75%
No. of court rooms with computer system	Int	1,200	1,043	87%	87%
No. of court rooms with speech-to-text	Int	1,200	701	58%	58%

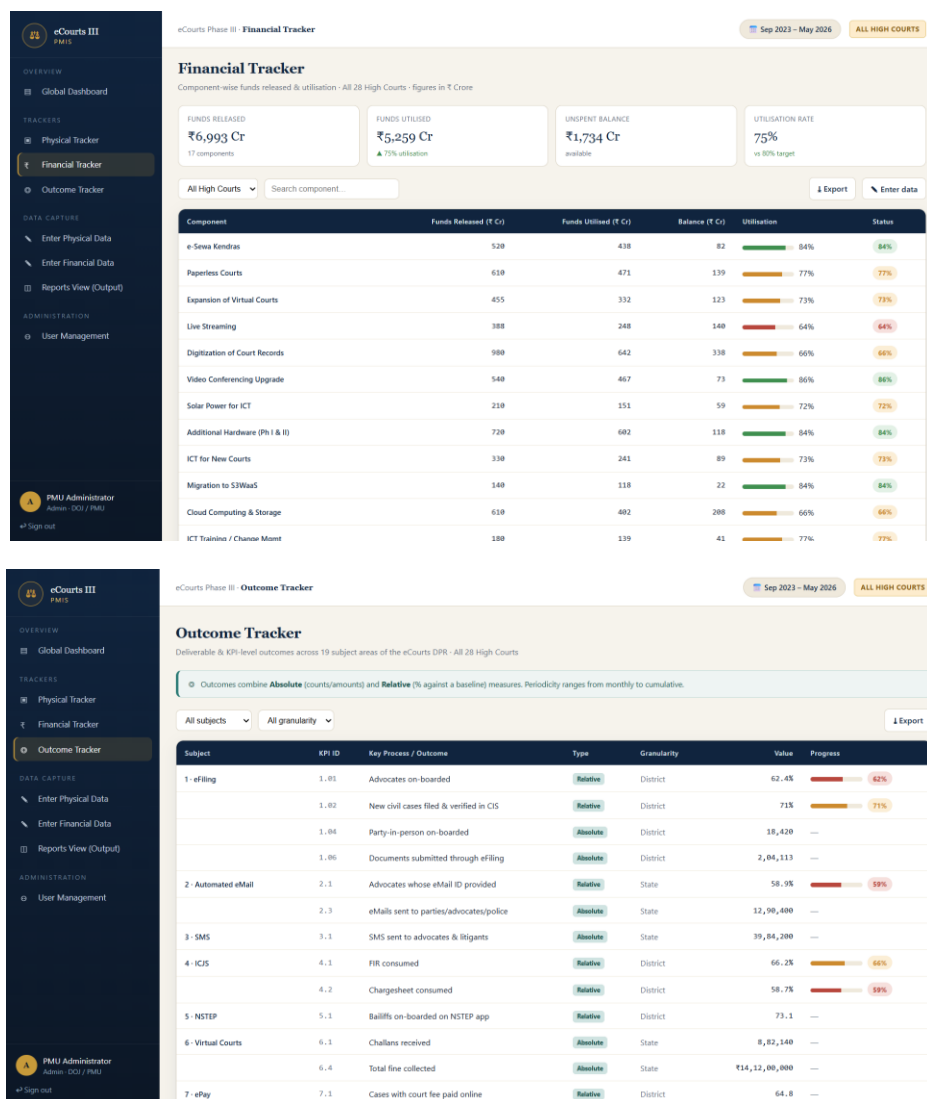

9.2 Filters & Interaction

- Filters on every report: Reporting Month (default = latest available), High Court (Admin/Viewer only; CPC locked to own), Component / Subject, and - for Outcome — Granularity.
- Tables are sortable on any column and support search within indicator / KPI text.
- Month-over-month comparison is available so fund absorption and physical progress trends can be tracked over time.
- Export:** every report view exports to Excel and PDF, honouring the active filters and the user's jurisdiction scope.

9.3 Scope Enforcement in Reports

Every report query is filtered by the signed-in user's role and jurisdiction before results are returned. A CPC export therefore contains only their own High Court's rows - scope is enforced server-side, not merely hidden in the interface.

10. Non-Functional Requirements

Category	Requirement
Data Refresh	Submitted data is reflected in PMIS reports within a few minutes, together with the submitting user and edit date-time.
Performance	A full tracker report (28 High Courts × 17 components) loads within 5 seconds.
Security	Role-based access per Section 8; standard PMIS login; data encrypted in transit.
Audit Trail	All changes logged with user, timestamp, field, old value and new value; logs retained for the full scheme duration.
Browser Support	Latest Chrome, Edge and Firefox; desktop and tablet layouts.
Scalability	Structure extensible to District Courts and new components / indicators / KPIs without redesign.
Availability	Designed for use across all 28 High Courts concurrently during monthly reporting windows.

11. Key Assumptions & Dependencies

- All figures in the companion wireframe / prototype are for design reference only and do not represent actual scheme data.
- The official list of 28 High Court reporting units will be shared by e-Committee before master data is set up.
- The full indicator catalogue (Physical) and KPI master (Outcome) - including data types, baselines and periodicity - will be supplied as master data before go-live.
- Data-entry ownership is fixed as: **CPC enters all values for their own High Court; Admin may enter or override any High Court.**
- Data is structured in two layers - a single baseline entry for Sep 2023 to May 2026, and month-wise entries from Jun 2026 onwards.
- No new tool or platform is procured; the PMIS is configured within existing infrastructure.
- The Global Dashboard is specified and delivered separately; this BRD only guarantees the data structures it will consume.
- If access to the e-Committee's internal database (iJuris) is made available, manual data-collection effort can be reduced significantly. *Indicated by the Joint Secretary (Client); to be confirmed.*

12. Glossary

Term	Meaning
PMIS	Project Monitoring Information System — the tool specified in this BRD.
PMU	Project Monitoring Unit monitoring eCourts Phase III implementation.
DoJ	Department of Justice, Government of India — sanctioning authority.
e-Committee	e-Committee of the Supreme Court of India — oversees ICT enablement of the judiciary.
CPC	Central Project Coordinator — High Court nodal user; scoped to own High Court.
HC	High Court.

Term	Meaning
RBAC	Role-Based Access Control.
RAG	Red / Amber / Green status based on % thresholds.
UoM	Unit of Measure — the metric used to count Target / Achieved or a KPI value.
KPI	Key Performance Indicator (Outcome Tracker).
Absolute / Relative	Outcome measure type — a direct count/amount, or a value against a baseline.
Cr	Crore (₹ 1 Crore = ₹ 10,000,000).
NSTEP	National Service and Tracking of Electronic Processes.
S3WaaS	Secure, Scalable & Sugamya Website as a Service — GoI website-hosting platform.
ICJS	Inter-operable Criminal Justice System.
iJuris	Internal data platform of the e-Committee, Supreme Court of India.

ANNEXURE 1

Period	High Court Total 28	Component	Description	Data Type	Validation	Target	Achieved
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	e-Sewa Kendras	No of sites prepared (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	e-Sewa Kendras	No of e-sewa kendras in court complexes (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	e-Sewa Kendras	No of e-sewa kendra functional (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	e-Sewa Kendras	No of e-sewa kendras Setup with Porta cabin (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	e-Sewa Kendras	No of e-sewa kendras Setup within existing court complex space instead of porta cabin (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	e-Sewa Kendras	No of e-sewa kendras Provided with functional internet (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Paperless Courts	No of paperless courts (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Paperless Courts	No of court rooms with VC enabled (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Paperless Courts	No of court rooms with Led Display (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Paperless Courts	No of court rooms with Scanner Depoloyed (in Absolute Count)	Int	in Absolute Count (Numbers)		

Period	High Court Total 28	Component	Description	Data Type	Validation	Target	Achieved
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Paperless Courts	No of court rooms with Computer system installed (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Paperless Courts	No of court rooms with Speech to text enabled (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Expansion of Virtual Courts	No of sites prepared (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Expansion of Virtual Courts	No of virtual courts operational (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Expansion of Virtual Courts	No of court rooms with VC enebled (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Expansion of Virtual Courts	No of court rooms with Led Display (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Expansion of Virtual Courts	No of court rooms with Scanner Depoloyed (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Expansion of Virtual Courts	No of court rooms with Computer system installed (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Expansion of Virtual Courts	No of court rooms with Speech to text enabled (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Live Streaming	No of sites prepared (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Live Streaming	No of virtual courts operational (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 –	<Name of the High Court/High	Live Streaming	No of court rooms with VC enebled	Int	in Absolute Count (Numbers)		

Period	High Court Total 28	Component	Description	Data Type	Validation	Target	Achieved
May 2026	Court Bench>		(in Absolute Count)				
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Live Streaming	No of court rooms with Led Display (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Live Streaming	No of court rooms with Scanner Depoloyed (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Live Streaming	No of court rooms with Computer system installed (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Live Streaming	No of court rooms with Speech to text enabled (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Live Streaming	No of document visualiser installed (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Digitization of entire court records	No of pages digitized (in Cr.)	float	in Cr.		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Digitization of entire court records	No of pages(of active cases) digitized (in Cr.)	float	in Cr.		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Digitization of entire court records	No of pages(of legacy cases) digitized (in Cr.)	float	in Cr.		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Video Conferencing upgrade	No of video conference units installed (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Video Conferencing upgrade	No of video conference units functionals (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Video Conferencing upgrade	No of video conference installed in district govt hospitals	Int	in Absolute Count (Numbers)		

Period	High Court Total 28	Component	Description	Data Type	Validation	Target	Achieved
			(in Absolute Count)				
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Video Conferencing upgrade	No of video conference installed in Jails (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Video Conferencing upgrade	No of video conference installed in Courts +DSA (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Solar power for ICT infrastructure	No of solar pannels installed	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Additional hardware (Phase I & II replacement)	No of Courts upgraded with new infrastructure (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	ICT infrastructure for newly set-up courts	No of new Courts (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Migration of HC & District Court websites to S3WaaS	No of District Court websites migrated (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Migration of HC & District Court websites to S3WaaS	No of visitors to the migrated District Court websites (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Cloud computing & storage	Total centralised storage capacity (in PB)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	ICT Training / Change Management	No of training programmes conducted (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	NSTEP expansion across States/Uts	No of Court Establishments covered (in Absolute Count)	Int	in Absolute Count (Numbers)		

Period	High Court Total 28	Component	Description	Data Type	Validation	Target	Achieved
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	NSTEP expansion across States/Uts	No of hand held devices deployed (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Software Development	No of technical support team member recruited	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Project Monitoring Unit (PMU) in e-Committee and DOJ.	Percentage of project targets achieved (in %)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Connectivity (Primary + Redundancy)	No of New Court Complexes Connected through WAN (in Absolute Count)	Int	in Absolute Count (Numbers)		
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	e-Office for High Courts & District Courts	No of Courts implemented e-office (Absolute Count)	Int	in Absolute Count (Numbers)		

ANNEXURE 2

Period	High Court Total 28	Component	Description	Data Type	Validation
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	e-Sewa Kendras	Number of e-sewa kendras in court complexes (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Paperless Courts	Number of paperless courts (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Expansion of Virtual Courts	Number of virtual courts (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Live Streaming	Number of Courts (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Digitization of entire court records	Number of pages digitized (in Cr.)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Video Conferencing upgrade	Number of video conference (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Solar power for ICT infrastructure	Total units of power generated (kWH)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Additional hardware (Phase I & II replacement)	Number of Courts (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	ICT infrastructure for newly set-up courts	Number of Courts (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Migration of HC & District Court websites to S3WaaS	Number of District Court websites (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Cloud computing & storage	Total centralised storage capacity (in PB)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	ICT Training / Change Management	Number of training programmes (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	NSTEP expansion across States/Uts	Number of Court Establishments. (in Absolute Count)	Float	in Absolute Count (In CR)

Period	High Court Total 28	Component	Description	Data Type	Validation
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Software Development	Number of receipts (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Project Monitoring Unit (PMU) in e-Committee and DOJ.	Percentage of project targets achieved (in %)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	Connectivity (Primary + Redundancy)	Number of Court Complexes (in Absolute Count)	Float	in Absolute Count (In CR)
Sep 2023 – May 2026	<Name of the High Court/High Court Bench>	e-Office for High Courts & District Courts	Number of e-office installation. (in Absolute Count)	Float	in Absolute Count (In CR)

Note: Apart from the 17 components, a one-time amount of Rs. 23.3 Cr has been released to IIT Madras for Knowledge Management.

ANNEXURE 3

Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
1	eFiling	1.01	How many advocates are on-boarded	Relative	Bar Enrolled Advocates	Cumulative end of month	Percentage	District
		1.02	Number of New Cases Filed and verified in CIS [Civil]	Relative	Total Civil Institution	Monthly	Percentage	District
		1.03	Number of New Cases Filed [Criminal Private Complaints]	Relative	Total Criminal Private Institution	Monthly	Percentage	District
		1.04	How many party in person are on-boarded	Absolute		Cumulative end of month	Count	District
		1.05	No of New cases filed and verified in CIS by party in person	Relative	Number of New Cases Filed and verified in CIS [Civil]	Monthly	Percentage	District
		1.06	No of Documents submitted through efiling	Absolute		Monthly	Count	District

Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
		1.07	No of Oaths recorded through eFiling	Relative	Number of New Cases Filed in Month	Monthly	Count	District
		1.08	No of IAs filed through eFiling	Absolute		Monthly	Count	District
		1.09	No of digital payment transactions through eFiling	Absolute	Number of New Cases Filed in Month	Monthly	Count	District
		1.1	Value of digital payment transactions through eFiling	Absolute		Monthly	Amount	District
		1.11	No of eSigned Documents submitted through eFiling	Relative	No of Documents submitted through eFiling	Monthly	Percentage	District
2	Automated eMail	2.1	Number of Advocate whose eMail ID is provided	Relative	Number of Active Advocates with Bar Enrolment	Cumulative end of month	Percentage	State

Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
					Registered in CIS			
		2.2	Number of Parties in current Pending Cases whose eMail ID is furnished	Relative	Number of Parties in current Pending Cases	On a given date	Percentage	District
		2.3	No of emails sent to Parties, Advocates and Police Station per month	Absolute		Monthly	Absolute	State
3	SMS	3.1	SMS sent to Advocates and Litigants per month	Absolute	Count	Monthly	Absolute	State
		3.2	Number of Advocate whose Mobile number is provided	Relative	Number of Active Advocates with Bar Enrolment Registered in CIS	Cumulative end of month	Percentage	State
		3.3	Number of Parties in current Pending Cases whose Mobile number is provided	Relative	Number of Parties in current Pending Cases	On a given date	Percentage	District

Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
		3.4	Number of Pull SMS sent	Absolute	Count	Monthly	Absolute	National
4	ICJS	4.1	FIR Consumed	Relative	Total Pretrial cases registered	Monthly	Percentage	District
		4.2	Chargesheet Consumed	Relative	Total no of criminal cases [Police Challans] registered	Monthly	Percentage	District
		4.3	FIR Verified	Relative	FIR Consumed	Monthly		District
		4.4	Chargesheet Verified	Relative	Chargesheet Consumed	Monthly		District
		4.5	Digitally signed FIR received	Relative	FIR Consumed	Monthly	Percentage	District
		4.6	Digitally signed chargesheet received	Relative	Chargesheet	Monthly	Percentage	District

Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
					Consumed			
		4.7	Accused with email id in charesheet received through ICJS	Relative	Total no of accused in criminal cases registered based on chargesheet	Monthly	Percentage	District
		4.8	Witness with email id in charesheet received through ICJS	Relative	Total no of witness in criminal cases registered based on chargesheet	Monthly	Percentage	District
5	NSTEP	5.1	Total no of bailif onboarded on NSTEP mobile app	Relative	Total no of bailifs	Cumulative end of month	Count	District

Subj ect ID	Subject	KPI D	Key Process	Outco me [Absol ute/ Relativ e]	Base Line	Periodi city	Value	Granulari ty- State/Dis trict
		5.2	Total no of Civil process published	Absolut e		Monthl y	Count	District
		5.3	Total no of Civil process allocated to bailif	Relative	Total no of Civil process publishe d	Monthl y	Percent age	District
		5.4	Total no of Civil process served by bailif	Relative	Total no of Civil process allocated to bailif	Monthl y	Percent age	District
		5.5	Total no of Criminal process published	Absolut e		Monthl y	Count	District
		5.6	Total no of criminal process served through Police/ICJS	Relative	Total no of Criminal process publishe d	Monthl y	Count	District
		5.7	No of summons and notices sent through email in Civil	Relative	Total no of Civil process publishe d	Monthl y	Count	District
		5.8	Authentication received for summons and notices sent through email	Relative	No of summon	Monthl y	Count	District

Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
					s and notices sent through email			
		5.9	No of summons and notices sent through email in Civil	Relative	Total no of Criminal process published	Monthly	Count	District
		5.1	Authentication received for summons and notices sent through email	Relative	No of summons and notices sent through email	Monthly	Count	District
6	Virtual Courts	6.1	Challans Received	Absolute		Monthly	Count	State
		6.2	Proceeding Completed In Cases	Absolute		Monthly	Count	State
		6.3	No of Cases in which Fine Paid	Absolute		Monthly	Count	State
		6.4	Total Fine Collected	Absolute		Monthly	Amount	State

Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
		6.5	Violaters Contested the Case	Absolute		Monthly	Count	State
7	ePay	7.1	Number of Cases in which Court Fee is Paid online	Relative	Number of Cases Filed	Monthly	Count	District
		7.2	Value of digital payment transactions for Court Fees	Absolute		Monthly	Value	District
		7.3	Number of Cases in which Fine is Paid online	Relative	Number of Criminal Cases Disposed and in which Fine is imposed	Monthly	Count	District
		7.4	Value of digital payment transactions for Fine	Absolute		Monthly	Value	District
		7.5	Number of Cases in which Penalty is Paid online	Absolute		Monthly	Count	District
		7.6	Value of digital payment transactions for Penalty	Absolute		Monthly	Value	District
		7.6	Number of Cases in which Judicial Deposit is Paid online	Absolute		Monthly	Count	District
		7.7	Value of digital payment transactions for Judicial Deposits	Absolute		Monthly	Value	District

Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
8	Mobile app	8.1	No of Android Downloads	Absolute		Monthly	Count	National
		8.2	No of iOS Downloads	Absolute		Monthly	Count	National
		8.2	Case Status Accessed (Mobile App)	Absolute		Monthly	Count	National
		8.3	No. of Orders Accessed (Mobile APP)	Absolute		Monthly	Count	National
		8.4	Updating Current Status (Mobile App)	Absolute		Monthly	Count	National
		8.5	Causelist Accessed (Mobile App)	Absolute		Monthly	Count	National
9	Video conferencing	9.1	Total no of hearing conducted through VC Civil	Relative	Total no of hearings	Monthly	Count	District
		9.2	Total no of hearing conducted through VC Criminal	Relative	Total no of hearings	Monthly	Count	District
		9.3	Total no of downtime incidents	Absolute		Monthly	Count	District
10	JustIS mobile app	10.1	No. of JOs onboarded	Relative	Number of JOs	Cumulative end of month	Count	District
11	NAPIX	11.1	State departments	Absolute		Monthly	Count	National

Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
		11.2	Central departments	Absolute		Monthly	Count	National
12	DC services portal	12.1	No of final orders and judgements uploaded	Absolute	No of cases disposed	Monthly	Count	District
		12.2	Total no of Digitally signed orders and Judgements	Relative	No of final Orders and Judgments	Monthly	Percentage	District
		12.3	Causelist Accessed	Absolute		Monthly	Count	National
		12.4	No. of Orders Accessed	Absolute		Monthly	Count	National
		12.5	Case Status Accessed	Absolute		Monthly	Count	National
		12.6	Caveat Status	Absolute		Monthly	Count	National
13	eSewa Kendra	13.1	Case Status Query	Relative	Pendency	Monthly	Count	District
		13.2	Availing Video Conferencing Facility	Relative	Pendency	Monthly	Count	District
		13.3	Availing eFiling Facility	Relative	Pendency	Monthly	Count	District
		13.4	Availing Virtual Court Facility	Relative	Pendency	Monthly	Count	District

Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
		13.5	Availing Online Payment Facility	Relative	Pendency	Monthly	Count	District
14	Digitization of Case Records	14.1	Number of Cases Digitized	Relative	Total Records Digitized	Monthly	Count	District
		14.2	Number of storage consumed (in PB)	Absolute		Monthly	Count	State
15	Solar Facilities	15.1	Monthly Generation of Electricity in KWH through Solar Facility	Absolute		Monthly	Count	District
		15.2	Percentage of Electricity utilized in the courts through Solar Facility	Relative	Monthly Consumption of Electricity in total	Monthly	Percentage	District
16	eOffice	16.1	Number of Staff on-boarded on eOffice	Relative	Number of Staff	Monthly	Percentage	State
		16.2	Number of eFiles Processed	Absolute		Monthly	Count	State
		16.3	Number of receipts in eOffice	Absolute		Monthly	Count	State
17	Touch Screen Kiosks	17.1	Number of Touch Screen Kiosks Installed	Relative	Number of Pending Cases [Footfalls]	Yearly	Ratio	District


Subject ID	Subject	KPI D	Key Process	Outcome [Absolute/Relative]	Base Line	Periodicity	Value	Granularity-State/District
18	Change Management	18.1	Number of Judicial Officers Trained	Relative	Number of Judicial Officers	Monthly	Percentage	State
		18.2	Number of Staff Trained	Relative	Overall Number of Staff	Yearly	Percentage	District
		18.3	Number of Advocates Trained	Relative	Advocates	Yearly	Percentage	State
		18.4	Number of Training Hours	Absolute		Monthly	Count	State
19	Paperless Courts	19.1	Number of cases Disposed through paperless courts	Absolute		Monthly	Count	State

ANNEXURE 4

LIST OF HIGH COURTS

S. No.	High Court Name
1	Allahabad High Court
2	Andhra Pradesh High Court
3	Bombay High Court
4	Calcutta High Court
5	Chhattisgarh High Court
6	Delhi High Court
7	Gauhati (Assam) High Court
8	Gauhati (Arunachal Pradesh) High Court
9	Gauhati (Mizoram) High Court
10	Gauhati (Nagaland) High Court
11	Gujarat High Court
12	Himachal Pradesh High Court
13	Jammu & Kashmir High Court
14	Jharkhand High Court
15	Karnataka High Court
16	Kerala High Court
17	Madhya Pradesh High Court
18	Madras High Court
19	Manipur High Court
20	Meghalaya High Court
21	Orissa High Court
22	Patna High Court
23	Punjab & Haryana High Court
24	Rajasthan High Court
25	Sikkim High Court
26	Telangana High Court
27	Tripura High Court
28	Uttarakhand High Court

GLOBAL DASHBOARD

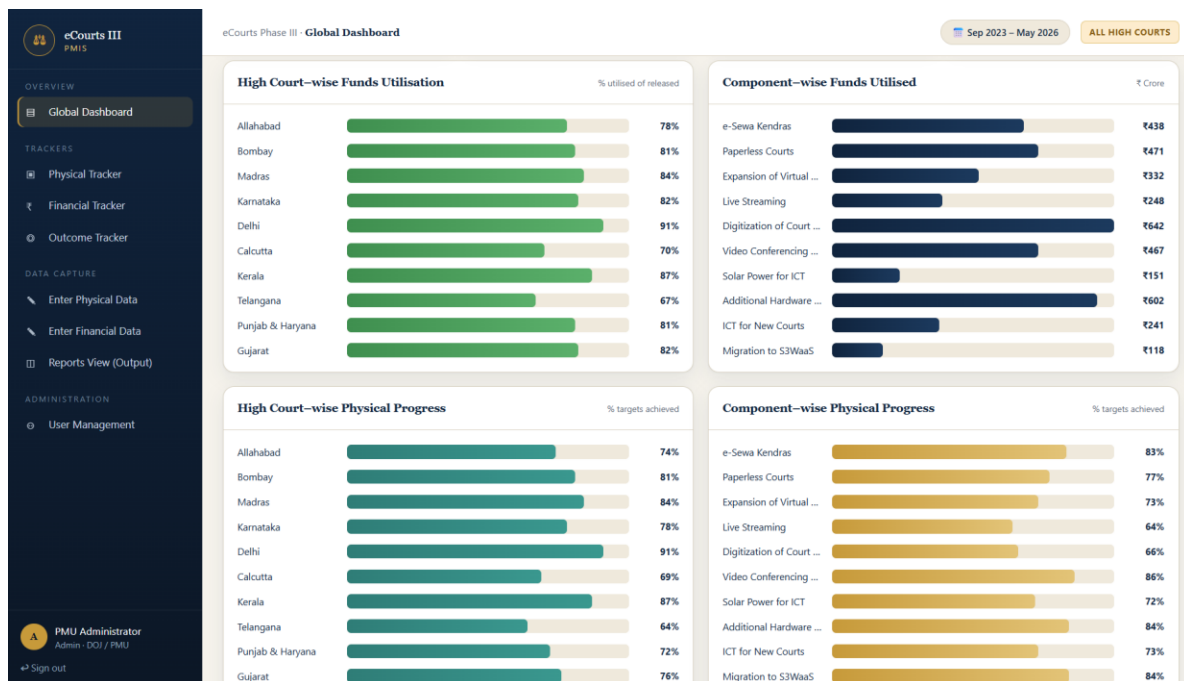


eCourts III
PMU'S

Overview
Global Dashboard
Trackers
Physical Tracker
Financial Tracker
Outcome Tracker
Data Capture
Enter Physical Data
Enter Financial Data
Reports View (Output)
Administration
User Management


PMU Administrator
Admin / DOJ / PMU
Sign out

eCourts Phase III - Reports View

Sep 2023 - May 2026

All High Courts


Reports View (Output)

How data appears to viewers - read-only - High Court of Karnataka

This is the **output / viewing** layer. Viewers (read-only role) see published figures and reports but cannot edit, delete or modify any value.

Financial Snapshot

High Court of Karnataka - ₹ Cr



Funds Released	1402
Funds Utilised	1331
Balance	771

Overall Physical Progress

component summary

e-Sewa Kendras		83%
Paperless Courts		77%
Expansion of Virtual ...		73%
Live Streaming		64%
Digitization of Court ...		66%
Video Conferencing ...		86%

e-Sewa Kendras — Indicator Outputs

read-only

No. of sites prepared

366 / 420 target

87% achieved - 87%

No. of e-sewa kendras in court complexes

341 / 390 target

87% achieved - 87%

No. of e-sewa kendras functional

318 / 390 target

82% achieved - 82%

No. of e-sewa kendras set up with porta cabin

121 / 150 target

81% achieved - 81%

No. of e-sewa kendras within existing complex

197 / 240 target

82% achieved - 82%

No. of e-sewa kendras with functional internet

329 / 390 target

84% achieved - 84%
